


The background features a dark navy blue rectangular area with a repeating pattern of concentric circles. This central area is surrounded by an abstract composition of organic, flowing shapes in shades of blue, brown, orange, and cream, some of which contain fine line patterns.

ORACLE NETSUITE

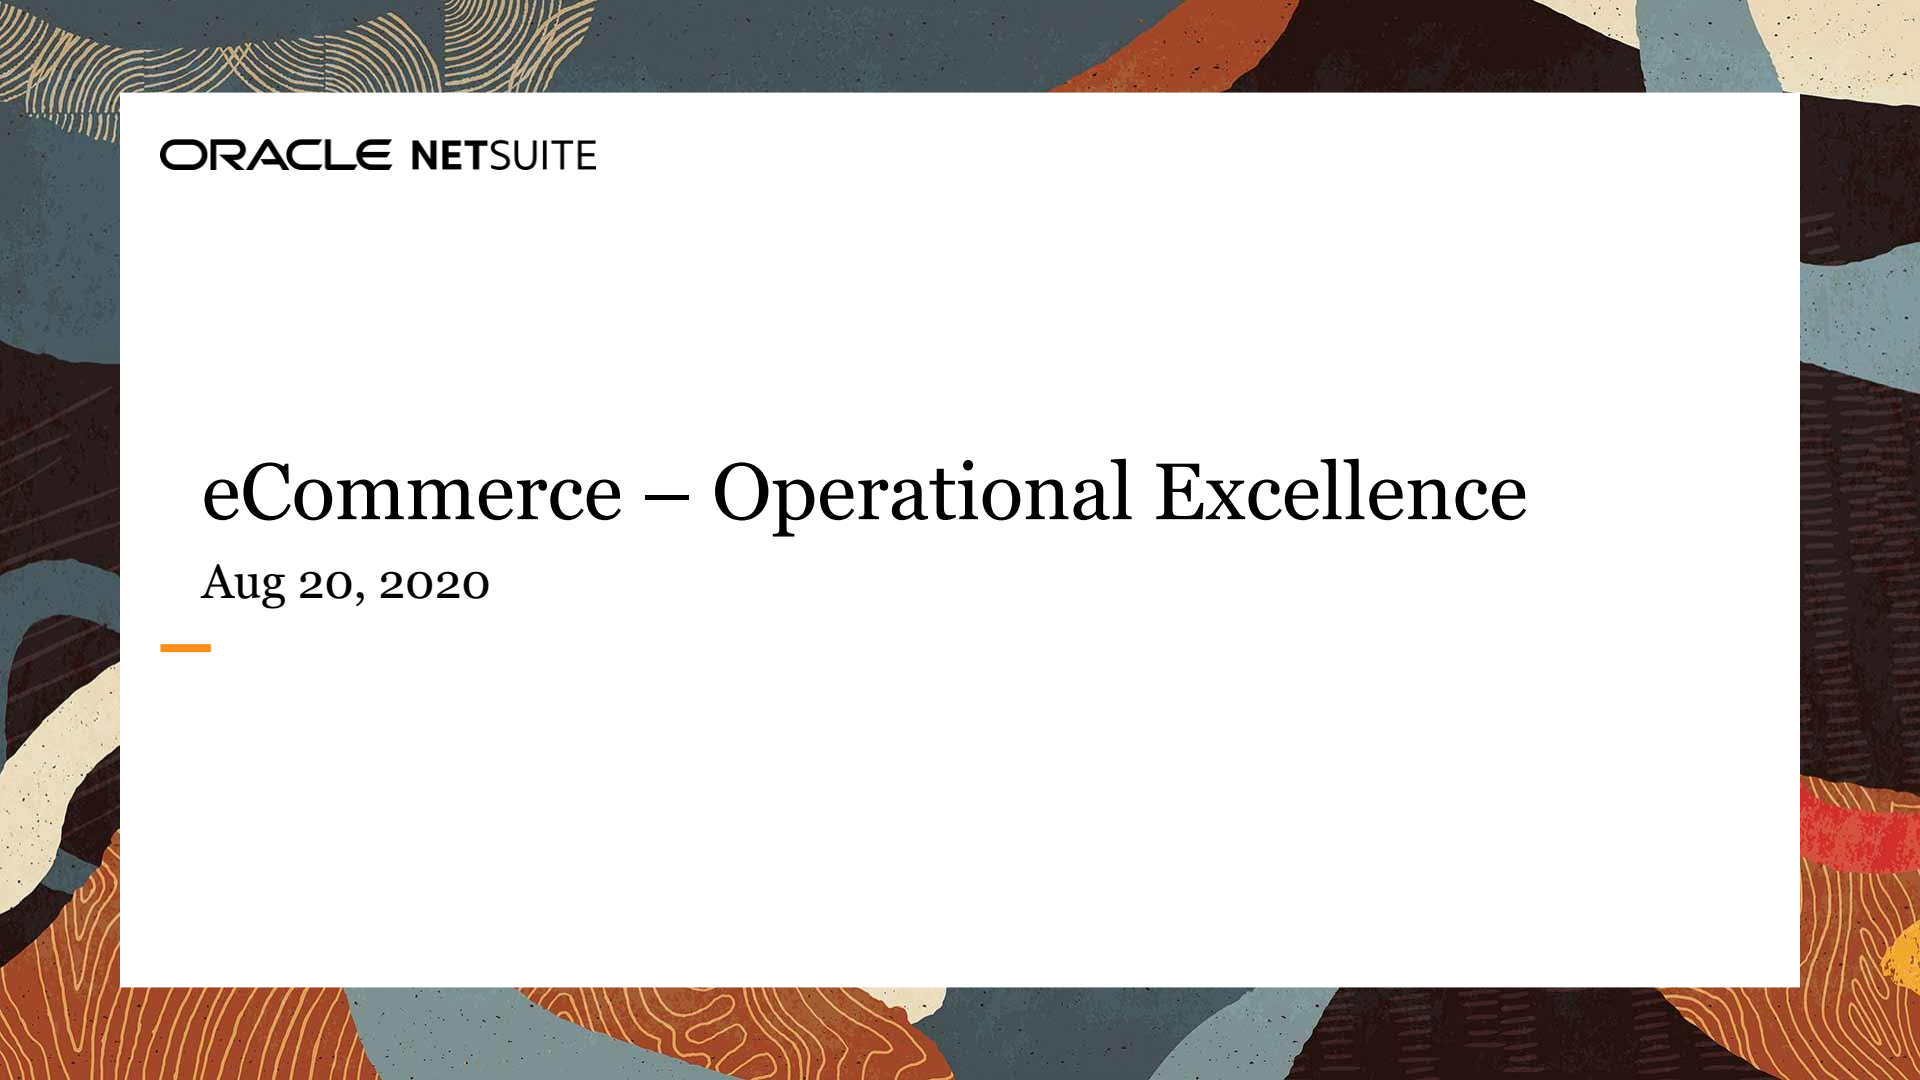

ORACLE NETSUITE

eCommerce – Operational Excellence

Aug 20, 2020

Topics



- 1 Jira Guidelines
- 2 Forecasting Guidelines
- 3 Time Entry Guidelines
- 4 Budget Management Guidelines

The two things...

1 When in doubt, ask (don't assume)



2 Everyone's key for our processes to work





Jira Guidelines

Jira Guidelines



1. Reflecting our work in Jira
2. Ownership and status of customizations
3. Reflect the status of tasks
4. Planning & Prioritization
5. Weekly deadlines and responsibilities
6. Reference documentation
7. Next Steps

Reflecting our work in Jira


Expectation #1: Jira is the primary source of truth for reflecting our work

- ✓ Delivery Managers need to create an Epic in Jira to represent a project and assign it to the PM (or PM/FC)
- ✓ Functional Consultants will create the list of customizations and corresponding FC, Dev, and QA tasks (per the information provided by the PC). The timing of backlog creation depends on the project size:
 - ✓ For projects with a large number of customizations, wait until the Kick-off call for scope alignment w/customer
 - ✓ For all other projects, the backlog can be created as soon as the team is assigned to the Job
- ✓ If more granular tasks are needed, every team member can create their own tasks under each customization

Ownership and status of customizations

Expectation #2: Status and ownership of all customizations should be accurately represented

- ✓ There should always be one owner (GO-TO person) for a customization at any given time
- ✓ When a customization's ownership is transitioned, the previous assignee is responsible for re-assigning it
- ✓ When a customization's life cycle changes, the current owner is responsible for updating its state
- ✓ Every change to a customization's life cycle or ownership should be signaled through a comment with tagging

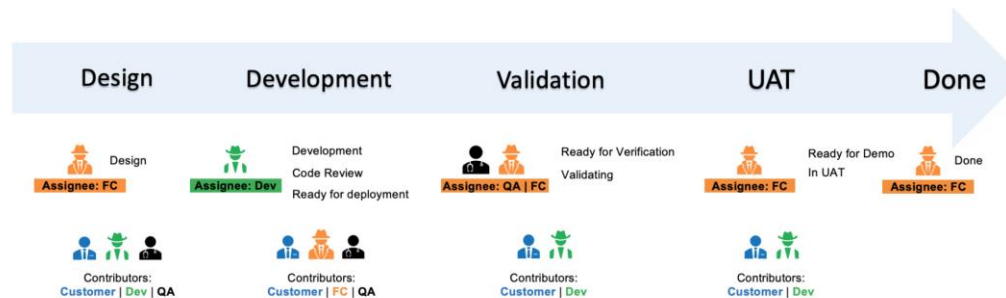

Reflecting the status of a task

Expectation #3: Every team member is responsible for updating their tasks as changes occur

- ✓ Task information to keep updated includes:
 - ✓ Assignee: Determines ownership
 - ✓ Life cycle state: Upcoming work | Waiting | Next Week | This Week | Current Work | etc.
 - ✓ Due date (when applicable)
 - ✓ Original estimate
 - ✓ Commentary to reflect changes or clarifications on the task or its expected completion
- ✓ Always tag the PM and FC (and any other affected team member) on a Jira comment when changes occur

Planning and prioritization of work

Expectation #4: Team members should honor prioritization and planning decisions for work

- ✓ FCs are responsible for signaling which tasks are ready to be tackled (all pre-requisites met)
- ✓ PMs are responsible for prioritizing those tasks and signaling accordingly
- ✓ PMS are responsible for signaling which tasks they expect to be tackled next week
- ✓ All team members are responsible for validating the timeline expectations and align with PMs as needed
- ✓ All team members are responsible for seeking more work should there assigned work be insufficient to meet their utilization target
- ✓ Changes to planned work should be communicated to the PM through a Jira comment (w/tagging)

Weekly deadlines and responsibilities

Expectation #5: Team members should comply with weekly deadlines for Jira updates


- ✓ **First thing on Mondays:** Reflect the current week's work on the Kanban board
 - ✓ Move all the "Next Week" column items to the "This Week" column
 - ✓ Confirm that you have hours assigned in NS Corp to cover for the planned work for the week
- ✓ **EOB Wednesdays:** Developers and FCs to ensure their assigned tasks and customizations are up-to-date
 - ✓ Validate that Original estimates correspond to the expected level of effort for tasks
 - ✓ Validate the feasibility of completion by established Due Dates (whenever specified)
 - ✓ Ensure all tasks and customizations are placed in their appropriate column in the Kanban board
 - ✓ Verify if any assigned customization should be transitioned to another team member, and reassign accordingly

Weekly deadlines and responsibilities (page 2)

- ✓ **EOB Thursdays:** PMs/FCs to update the tasks priorities, expected timing of execution and assignment
 - ✓ PMs should ensure all tasks are prioritized (when applicable)
 - ✓ PMs should move all tasks they expect to be tackled the following week to the "Next Week" column
 - ✓ FCs should identify all tasks from the backlog that are ready to be tackled, and move them to the "Upcoming work" column ("To do" state)
 - ✓ FCs should identify all unassigned tasks and assign appropriately
- **Fridays:** Developers and FCs should validate their Kanban board on **Friday mornings** and adjust their OpenAir forecast by **EOB Fridays**
 - Assess if tasks that may still be in the "Current Work" and "This Week" will be finished by Friday
 - Assess ability of completing in time all tasks set on the "Next Week" column
 - Should the tasks assigned for "Next Week" not be sufficient to fulfill your utilization goals, identify any tasks from your Upcoming work column, and **after aligning with the Project's PM and FC**, add move them to your next week column.

Weekly deadlines and responsibilities (page 3)

- ✓ **On an ad-hoc basis:** Reflect any changes to the planned work of the current week both in Jira and OpenAir as soon as you are aware of them
 - ✓ Should you become aware that there have been changes to the work planned for the current week, reflect those changes by moving the affected tasks to their respective column. It is expected that you will align with the FC and PM for the affected projects.
 - ✓ **Do not change your OpenAir forecast for the current week** to accommodate for the changes. The current week's forecast in OpenAir has already been committed to our vertical partners at this point, so it should not be altered. Only make changes, whenever applicable, to the following week, or any other week thereafter.



Forecasting Guidelines

Forecasting Guidelines



1. Forecast expectations
2. Including new work into the Forecast
3. Ongoing Forecasting and Weekly Maintenance
4. FAQs

Forecast Expectations



Expectation #1: Forecasting is an individual exercise

- ✓ Planning meetings aren't expected
- ✓ Communication is key, but last ownership is individual.
- ✓ YOUR goal is to be accurate and maximize your utilization.

Expectation #2: Communicate

- ✓ No work / Too much work: Say it beforehand!
- ✓ (PM/FC) a task is not happening "next week"? Raise the hand
- ✓ You are not confident about next week's work happening? Align for better outcome. Utilization is your own responsibility.
- ✓ Can't commit with what's planned (resource / project plan) according to forecast? Say it beforehand

Forecast Expectations

Expectation #3: Requirements

- ✓ Forecast must be updated every Friday EOD with the freshest info.
 - ✓ Next 2 weeks = mostly Jira
 - ✓ 3+ weeks = communication with the rest of the team, project plan (if applies), etc.
- ✓ Minimum of 6 weeks should be forecasted.
- ✓ Healthy forecast: (minimum) 6 weeks with 30+ billable hrs in.

Expectation #4: Ownership and Accountability

- ✓ You are the final owner of your forecast and utilization. Help yourself and our team to reach the goals! (70% 😊)

Including New Work

1- Staffing email

- ✓ Going forward main resources (PM/FC, main Dev) will be copied in RMO email.
- ✓ PM has to assign hours within 24 hrs from assignment.
- ✓ Pricing Calculator is a reference of hours per role → You must get all hours assigned at once.
- ✓ Define a high level tentative date between main resources → Include project on the forecast
- ✓ IF resource/project plan happens: align and update if needed.

2- Assigned as secondary resource or ad-hock tasks

- ✓ You may be asked to join a project after a resource plan is done, or for a given task.
- ✓ Ask for: estimated hours, estimated timeline, Jira tasks to be assigned if/when applicable and all hours assigned on the job.
- ✓ If the assignment is for next week or week after: It should be in Jira and forecast should reflect that.
- ✓ If it'll start 3+ weeks from the assignment: you should forecast based on timeline, and adjust later.

Ongoing Forecasting and Weekly Maintenance

Short term vs mid-long term forecasting – Weekly cadence

Friday	Week 1 (Next week)	Week 2	Week 3+
Forecasting for next weeks	• Accuracy: +95% hours (measured against the job) • Goal: Maximize Billable utilization through proper planning, visibility on utilization constraints. • Forecast mostly reflects Jira tasks. • Updated every Friday		• Accuracy: mostly reflects total hours and allocation in projects • Goal: plan utilization and allocation – gives time to raise the hand if no work/too much work • New projects should be included 3+Weeks ahead of time • Hours distribution mostly reflects project allocation and resourcing • Updated every Friday, either to reflect Jira or new updates (pushes, Project changes, etc)



Time Entry Guidelines

Time Entry Expectations

Expectation #1: Hours assigned at all time

- ✓ PM or FC/PM to assign hours from the beginning within a task (so it appears in OA)
- ✓ Make sure you have the hours assigned before getting started
- ✓ Make sure you have sufficient hours to keep your work going

Expectation #2: Submit (and approve) your time Daily

- ✓ One timesheet per day
- ✓ Submit and approve on a daily basis
- ✓ If we remove roadblocks, time tracking should take “5 mins” a day

SIDE NOTE: If you see anything preventing us from tracking time daily “with only 5 mins”, let us know!!

Time Entry Expectations

Expectation #3: Communicate (before doing)

- ✓ Hours aren't assigned and you have to get started soon
- ✓ You are not assigned to the job/task
- ✓ When a task will take more than original estimate
 - ✓ **Stop** working
 - ✓ Align with PM on new task estimate
 - ✓ If PM approves, keep going (PM can approve only if there's budget for it. No approval without hrs)



Budget Management Guidelines

Budget Management Expectations

Expectation #1: Job Management

- ✓ One task per role
- ✓ One task for Overage if needed

Expectation #2: Approval rules

- ✓ If within original estimate: Approve
- ✓ If not within original estimate and no prior communication: Ask questions and raise to management
- ✓ If a task goes over the estimate and the team is aligned that it needed to, and there are hours in the job: Go ahead and approve, don't wait until a formal overage is approved

Budget Management Expectations

Expectation #3: Overage Management

- ✓ Do as much as you can to accommodate within the budget before going for an overage
- ✓ Don't wait until you run out of hours to request the overage
- ✓ While one overage request is ideal, it is not forbidden to have more than one

Expectation #4: Overturning a job

- ✓ If the project ran out of hours and you get written confirmation on an overage
- ✓ If you are waiting for paperwork (CO signed and waiting for internal paperwork, overage approved but not yet reflected in job etc)
- ✓ Talk to leadership!

Budget Management Expectations



Expectation #5: Billable is Billable

- ✓ Don't log nor ask to log customer work against WWPS
- ✓ All hours must be logged daily. If something happens, approval can be hold until further discussion.

Expectation #6: Utilized Equivalent

- ✓ During a project: Should be used for not-in-scope estimates only
- ✓ Helping Sales



Resources

Resources



- ✓ [Jira Guidelines](#)
- ✓ [Forecasting Guidelines](#)
- ✓ [Time Entry Guidelines](#)



Q&A
